


GENERAL CONSTRUCTION SEQUENCE NOTES

- 1.) TIMBER WILL BE HARVESTED WITHIN PROJECT LIMITS UNDER ONE CUTTING. NO TREES ARE TO BE CUT WITHIN 25 FEET OF THE WETLAND EDGE, AND ALL TREES ARE TO BE FELLED AWAY FROM WETLANDS.
- 2.) MATERIALS REMOVAL, FINISH GRADING, LOAMING, AND SEEDING WILL BE ACCOMPLISHED IN STAGES TO MINIMIZE EROSION POTENTIAL. WORK AREAS WILL COMPRISE APPROXIMATELY ONE-ACRE INCREMENTS. NEW WORK AREAS WILL NOT BE INITIATED UNTIL PREVIOUS AREA HAS BEEN STABILIZED.
- 3.) ALL EXCAVATION, MATERIALS REMOVAL, AND HAULING WILL BE CONDUCTED BY THE APPLICANT, NOT BY OUTSIDE SOURCES.

LOCATION MAP

0 600
SCALE IN FEET

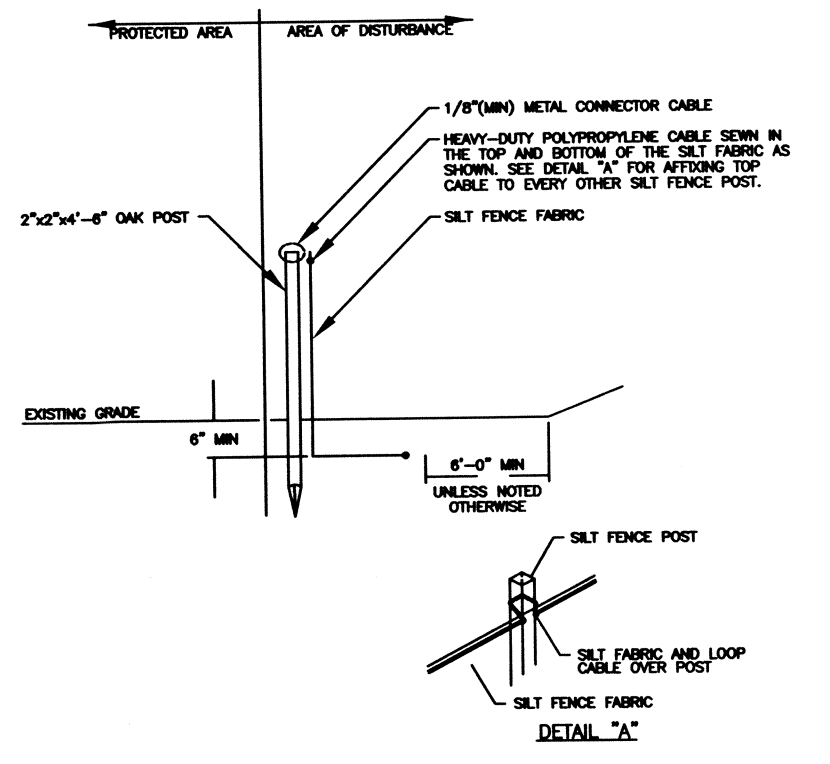

TRENCHED SILT FENCE

Paul's cell
508-958-1229


69-562

EROSION AND SEDIMENTATION CONTROL

- 1.) ALL PERIMETER EROSION AND SEDIMENTATION CONTROLS MUST BE INSTALLED PRIOR TO THE COMMENCEMENT OF EARTHWORK.
- 2.) ACCESSIBLE RESERVES OF HAY BALES AND STAKES ARE TO BE MAINTAINED ON SITE FOR ROUTINE MAINTENANCE AND IN THE EVENT OF UNANTICIPATED PROBLEMS REQUIRING EMERGENCY RESPONSE.
- 3.) HAY BALES SHOULD BE INSTALLED IN ACCORDANCE WITH THE DETAILS PROVIDED.
- 4.) NO WORK IS TO OCCUR ON THE WETLAND SIDE OF THE PERIMETER EROSION AND SEDIMENTATION CONTROLS. ALL PERIMETER CONTROLS SERVE AS THE PROJECT LIMIT OF DISTURBANCE.
- 5.) NO STONES, BRUSH, CONSTRUCTION DEBRIS, LITTER, OR OTHER MATERIALS ARE TO BE DEPOSITED ON THE WETLAND SIDE OF THE EROSION AND SEDIMENTATION CONTROLS.
- 6.) ALL DISTURBED SOILS NOT DESIGNATED FOR OTHER SURFACE TREATMENT ARE TO BE LOAMED AND SEEDED IMMEDIATELY FOLLOWING FINAL GRADING.
- 7.) APPROPRIATE PRECAUTIONS SHOULD BE TAKEN TO PREVENT THE TRANSPORT OF SOIL OFF SITE FROM FROM CONSTRUCTION EQUIPMENT.
- 8.) ALL PERIMETER EROSION AND SEDIMENTATION CONTROLS MUST BE PROPERLY MAINTAINED AND MUST REMAIN IN PLACE UNTIL THE SOILS HAVE BEEN STABILIZED TO THE SATISFACTION OF THE ENGINEER AND THE SECONK CONSERVATION COMMISSION.

NOTES:

- 1.) THIS PLAN DOES NOT REPRESENT A BOUNDARY LINE SURVEY.
- 2.) THE PURPOSE OF THIS PLAN IS FOR ESTABLISHING GRADES FOR FUTURE NURSERY STOCK.
- 3.) PROPOSED MATERIAL REMOVAL = 42,000 CY.



SITE PLAN
PREPARED FOR
PAUL & CONSTANCE MEDEIROS
WINDY ACRES NURSERY
149 CHESTNUT STREET
SEEKONK, MASSACHUSETTS

CAPUTO AND WICK LTD.
1150 PAWTUCKET AVE.
RUMFORD, R.I. 02916
401-434-8880

DATE
MARCH 30, 2005
REV. 4/11/05
SHEET
1
