Holden Public Safety Facility - Project Schedule

ID	Task Name	Duration	Start	Finish	Predeces
1		580 days	Wed 4/2/08	Tue 6/22/10	
2	Notice to Proceed	1 day	Wed 4/2/08	Wed 4/2/08	
3	**Schematic Design**	35 days	Thu 4/3/08	Wed 5/21/08	
4	**Building Plan Revisions**	28 days	Thu 4/3/08	Mon 5/12/08	
5	**Engineering Systems Review**	10 days	Wed 5/7/08	Tue 5/20/08	
6	**Committee Review**	1 day	Wed 5/21/08	Wed 5/21/08	5
7	**Design Development**	84 days	Thu 5/22/08	Tue 9/16/08	3
8	**Develop Building Plans**	40 days	Thu 5/22/08	Wed 7/16/08	
9	**MEP Engineering Development**	40 days	Thu 6/5/08	Wed 7/30/08	
10	**Develop Interior Design**	20 days	Thu 6/5/08	Wed 7/2/08	
11	**Develop Security/Technology Plans**	12 days	Thu 6/12/08	Fri 6/27/08	
12	**Site Landscape / Grading Plans**	20 days	Thu 5/22/08	Wed 6/18/08	6
13	**Site Engineering Development**	29 days	Thu 6/19/08	Tue 7/29/08	12
14	**Detailed Estimate**	15 days	Thu 7/31/08	Wed 8/20/08	8,9
15	**Review and Approval by Committ**	1 day	Thu 8/21/08	Thu 8/21/08	14
16	**MHD Permitting**	60 days	Thu 6/19/08	Wed 9/10/08	12
17	**Other Site Permitting**	35 days	Wed 7/30/08	Tue 9/16/08	13
18	**Construction Documents**	103 days	Thu 8/21/08	Mon 1/12/09	14
19	**Prequalify Bidders**	75 days	Wed 9/17/08	Tue 12/30/08	
20	**Develop Plans & Specifications**	75 days	Thu 8/21/08	Wed 12/3/08	
21	**Final Cost Estimate**	15 days	Thu 11/20/08	Wed 12/10/08	
22	**Incorporate Revisions**	15 days	Thu 12/11/08	Wed 12/31/08	21
23	**Final Coordination C D's**	5 days	Thu 1/1/09	Wed 1/7/09	22
24	**Contract Document Printing**	3 days	Thu 1/8/09	Mon 1/12/09	23
25	**Bidding**	41 days	Tue 1/13/09	Tue 3/10/09	18
26	**Bid Period**	30 days	Tue 1/13/09	Mon 2/23/09	
27	**Bid Opening**	1 day	Tue 2/24/09	Tue 2/24/09	26
28	**Bid Review /Award**	10 days	Wed 2/25/09	Tue 3/10/09	27
29	**Construction Administration**	335 days	Wed 3/11/09	Tue 6/22/10	25
30	**Mobilization**	15 days	Wed 3/11/09	Tue 3/31/09	
31	**Construction Period**	300 days	Wed 4/1/09	Tue 5/25/10	30
32	**Punch List**	19 days	Wed 5/26/10	Mon 6/21/10	31
33	**Occupancy**	1 day	Tue 6/22/10	Tue 6/22/10	32

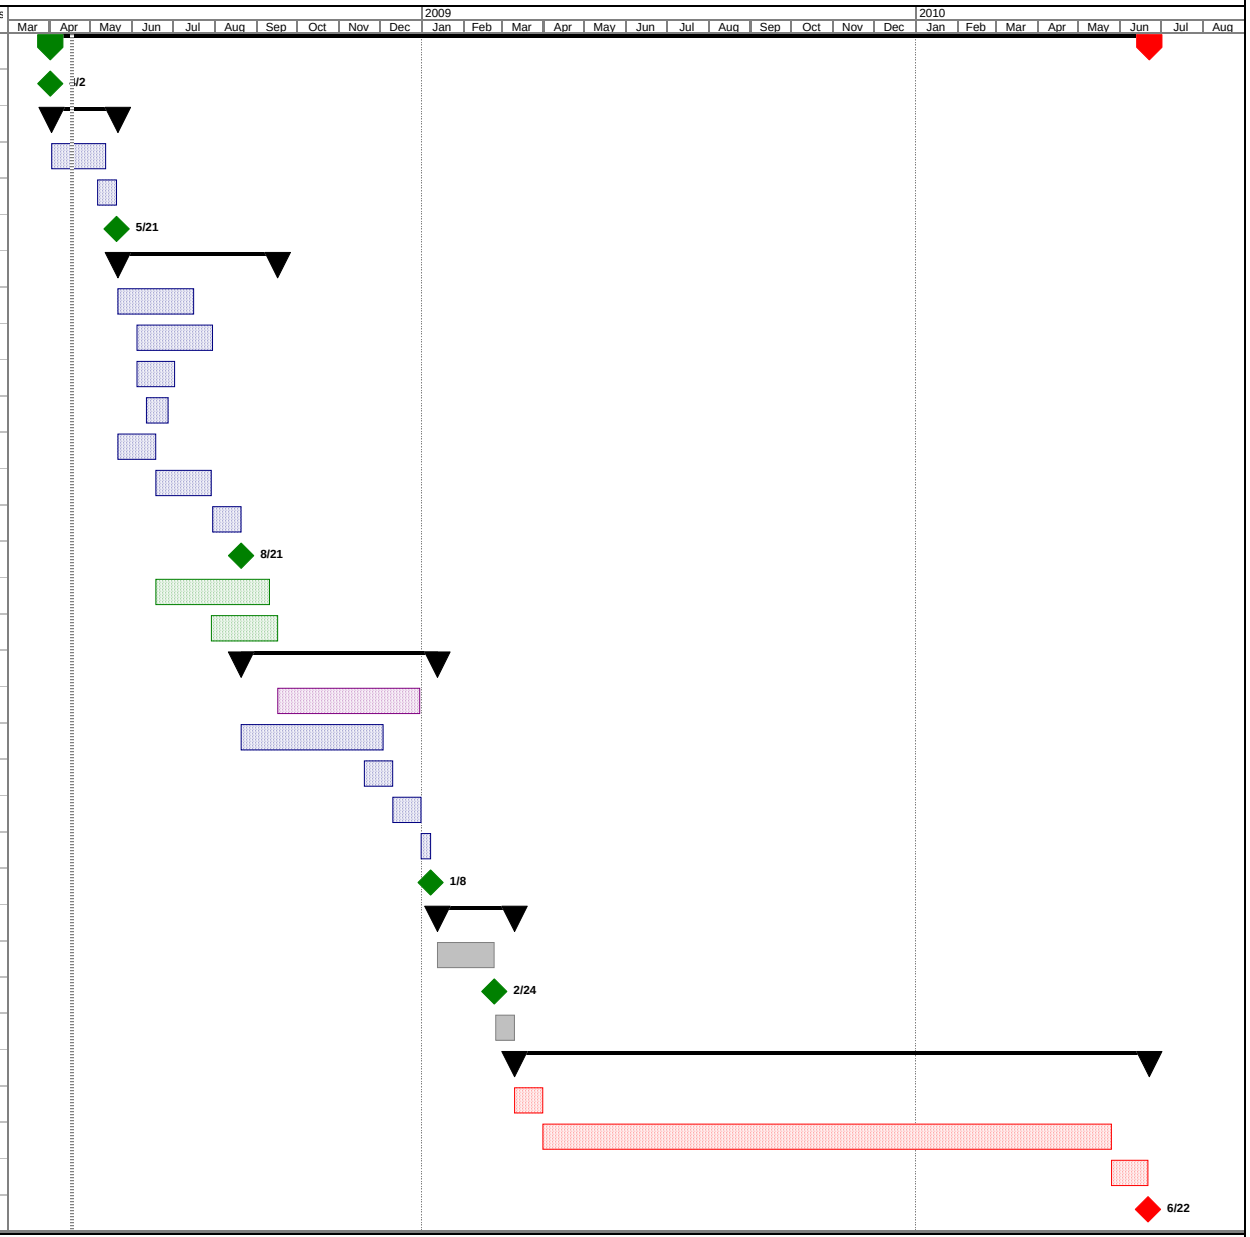

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
